Project2

ID	Task Name	Duration	Baseline Start	Baseline Finish	Start	Finish	Predecessors	Resource Names	Actual Cost
1	**ProjectEB13**	**30 days**	**Mon 9/12/16**	**Fri 10/21/16**	**Tue 9/13/16**	**Mon 10/24/1**			**$73,200.00**
2	Initiation	5 days	Mon 9/12/16	Fri 9/16/16	Tue 9/13/16	Mon 9/19/16		Shawn[80%],Nata	$6,800.00
3	Planning	10 days	Fri 9/16/16	Thu 9/29/16	Mon 9/19/16	Fri 9/30/16	2FS-1 day	Natasha[80%],Jef	$11,200.00
4	**Execution**	**6 days**	**Wed 9/28/16**	**Wed 10/5/16**	**Thu 9/29/16**	**Thu 10/6/16**	**3FS-2 days**		**$21,600.00**
5	Main page	3 days	Wed 9/28/16	Fri 9/30/16	Thu 9/29/16	Mon 10/3/16		Shawn[60%],Jeff[	$3,072.00
6	Catalog display	4 days	Wed 9/28/16	Mon 10/3/16	Thu 9/29/16	Tue 10/4/16		Liz[90%],Mike[90	$5,184.00
7	Database access	6 days	Wed 9/28/16	Wed 10/5/16	Thu 9/29/16	Thu 10/6/16	6SS	Natasha[70%],Kat	$5,280.00
8	Ordering page	4 days	Wed 9/28/16	Mon 10/3/16	Thu 9/29/16	Tue 10/4/16	6SS	Chad[70%],Jack	$4,800.00
9	Confirmation	3 days	Wed 9/28/16	Fri 9/30/16	Thu 9/29/16	Mon 10/3/16		Shawn[80%],Nico	$3,264.00
10	Procurement	5 days	Thu 10/6/16	Wed 10/12/1	Fri 10/7/16	Thu 10/13/16		Katie[50%]	$1,600.00
11	Testing	10 days	Thu 10/6/16	Wed 10/19/1	Fri 10/7/16	Thu 10/20/16	4	Shawn[70%],Jeff[	$28,640.00
12	Closing	2 days	Thu 10/20/16	Fri 10/21/16	Fri 10/21/16	Mon 10/24/1	11	Chad[90%],Nicole	$3,360.00



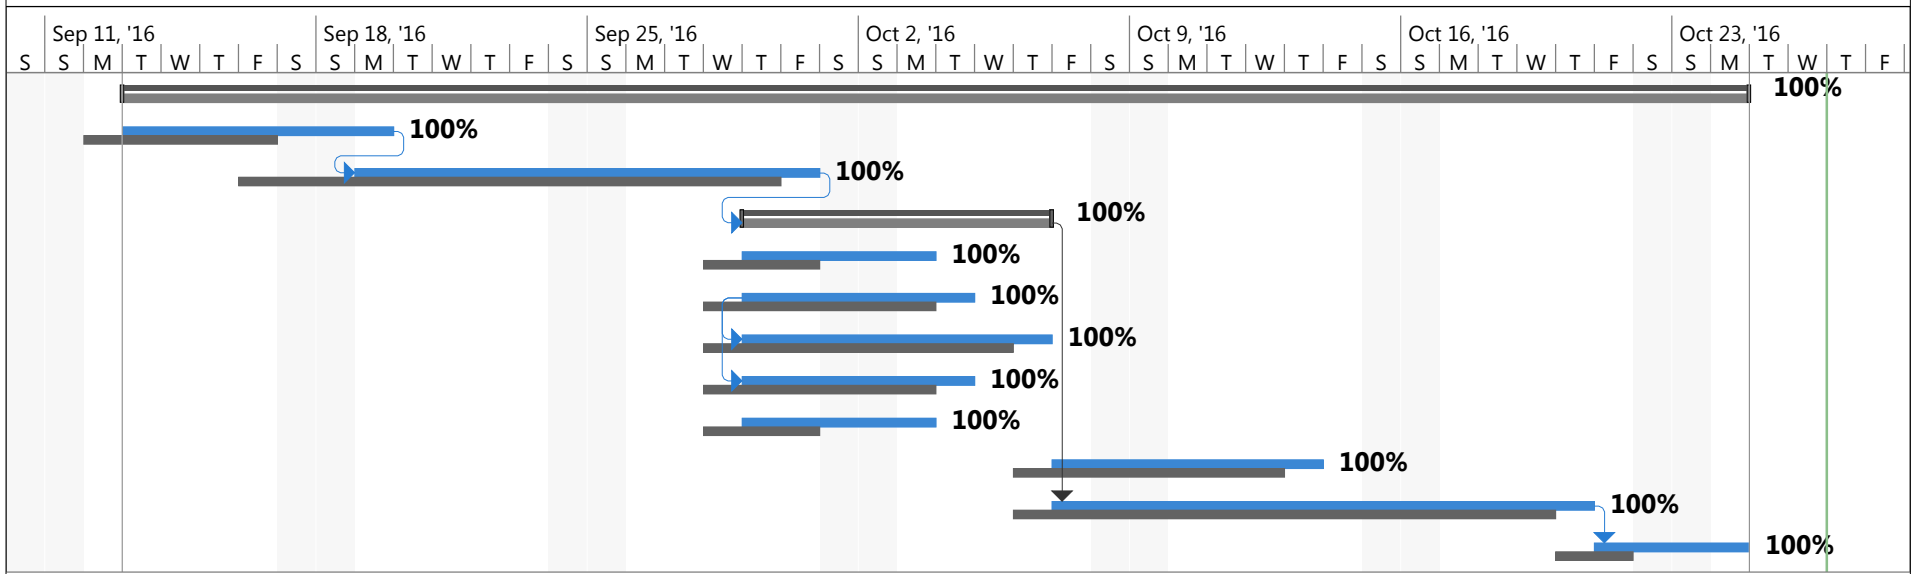

Critical		Finish-only		Manual Summary	
Critical Split		Duration-only		Project Summary	
Critical Progress		Baseline		External Tasks	
Task		Baseline Split		External Milestone	
Split		Baseline Milestone		Inactive Task	
Task Progress		Milestone		Inactive Milestone	
Manual Task		Summary Progress		Inactive Summary	
Start-only		Summary		Deadline	
